


H. D. SNOW and SON HOUSE MOVING, INC.

12155 BUSINESS HWY. 287 NORTH
FORT WORTH, TEXAS 76179



September 8, 2014

Wise County Sheriff Office
200 Rook Ramsey Drive
Decatur, TX 76234

Attn: Sgt. Blake Walls

Dear Sgt. Walls;

It is a pleasure to submit the following proposal to you for the relocation of the portable classroom building from Ft. Hood to Decatur, Texas.

These quotes are if we can reasonably place the building where you want it to be moved to:


- \$ 11,250.00 -- Cost to relocate portable classroom building
- \$ 350.00 -- Cost to remove underpinning
- \$ 1,000.00 -- Cost to install ten (10) anchors at new location
- \$ 1,450.00 -- Cost to install underpinning at new location, using same materials
- \$ 300.00 -- Cost to install treated 2 x 4's & rebar
- \$ 750.00 -- Cost to remove porch and haul to new location
- \$ 550.00 -- Cost to reinstall porch at new location
- \$ 925.00 -- Cost to bleed back air conditioner units, unhook from building & move to new location

H. D. Snow and Son House Moving Inc. will provide the State highway permit for this move.

If you have any questions, please call us anytime.

Sincerely,

Gary Snow, Vice President
H. D. Snow and Son House Moving Inc.



EAST TEXAS STRUCTURAL MOVERS

6419 fm 317 Athens Tx 75752
CELL: 903-386-8600 Office: 903-675-8300
ETSMWIDELOAD@GMAIL.COM

Wise County Sheriff's Office

Attn: Sgt. Blake Walls

Date: September 2, 2014

Subject: BID for Moving of 24x64 building located on Fort Hood, Tx.

ETSM will move: 24x64 building from Fort Hood to Decatur, Tx. ETSM will move building in one piece no interior electricity or plumbing will be cut or disconnected. ETSM **will not** disturb roof; and roof will not be opened up and exposed to the elements. ETSM will remove underpinning (skirting) from around building and place inside building. ETSM will not reinstall underpinning around building. ETSM will move the building to new location once arrived at new location ETSM will block and level building on blocks and pads no further than 6 feet apart. The extra added blocks and pads beneath the building will create a more stable and permanent foundation. Any extra materials will be furnished by Wise County Sheriff's office. An estimated cost of extra materials needed shall not exceed more than \$250.00. ETSM will remove porches and deliver to new location near Decatur, Tx. ETSM will not reinstall porches once delivered to new location. ETSM will disconnect air conditions and place inside building. ETSM will not reinstall air conditions. THIS BID IS GOOD FOR 30 DAYS.

Cost for moving of 24x64 building: \$10,500.00

Cost for removal of underpinning: \$200.00

Cost for removal and delivery of decks to new location: \$1,300.00

Sincerely,

A handwritten signature in cursive script that reads "Scott A. Shultz".

Scott A. Shultz

JUST RIGHT TRANSPORTATION SERVICES INC.

1440 FM 730 N, Azle, Texas 76020

Randy Martin – 817-444-6516/6533

Rebecca Martin - 817-757-0787

randymartin@peoplepc.com

To Prep the building:

1. Remove the skirting and reinstall skirting Cost: \$2,160.00
2. Disconnect the ac and reconnect the AC, Labor Cost : \$ 700.00 + Freon
3. Remove the porch load and unload and reset the the porch. Labor Cost: \$450.00
4. Disconnect the electricity and reconnect the electricity power available at the new site., set one pole, run wire up to 100 ft. buried in the ground. Cost \$4,000.00 . **Note this is from the pole we set not from the transformer and or running wire to the pole from the power company's source. If we have to deal with that that will be above the quote and be charge back to the client + 10% profit and 15% handling + Time.**
5. Remove and reinstall the awning Cost \$900.00 Labor + parts
6. Remove and re-install anchors parts and Labor Cost \$1600.00
7. Load out building on moving equipment beams and dollies , unblock, load blocking materials at the pick up site, Unload blocking materials at the new site, Un-load the building off the moving equipment and Block and level at new site with the existing materials, \$7,000.00 Note any extra blocking materials needed to complete the set-up is at the Clients expense. Cost Unkonwn
8. Transport the building up to 225 permitted miles using two private pilot cars, Transporting on movers equipment, dollies and Transport Rig Cost \$9,000.00
9. Note: This does not cover Law enforcement escorts if required by TX-DOT and or Mileage over 225 mi. Any thing over 225 mi will run \$40.00 per mile.
10. Furnish one TX-Dot Permit over size permit. Cost \$281.00
11. Out of town over night Cost for one night \$350.00
12. **Route inspection cost to drive out the route is \$600.00 cost to you if booked is Zero (000.00) for Badge discount. It is required by Law to obtain a moving permit.**

Note :No site work , Tree cutting for point A to Point B, Fence removal and re-installment is not part of this quote and if and of these services are furnished Cost is \$350.00 per. Hr. + materials.

The estimated Cost for the services above will run around Twenty six thousand and nighty one U.S. Dollars and No /100's (\$26,091.00)



DEFENSE LOGISTICS AGENCY

Disposition Services

Home | About Us | Public Affairs | Publications | FAQs | FOIA

Reutilization / Transfer / Donation (RTD) Requisition Item Details

Show reminder

Details for DTID: **W45NQ900490001**, Requisition Number: **2YTNUR42371410**

Current Request Status: Item being processed for release and shipment. The ESD is contained in rp 70-73 when provided in response to a follow-up.

[Return](#)

Inventory Information

Cycle:	<u>DOD</u>	Days Left in Cycle:	17	Hazardous:	<u>C</u>
Quantity Available:	1	Integrity Code:		Container ID:	
 Condition:	<u>A</u>	Site:	<u>DLA DS HOOD</u>	Orig. Acq. Price:	1,000.00
Item Name:	PREFABRICATED AND PORTABLE BUILDINGS	NSN:	5410DSBUILDIN	Date Entered Inv.:	05/13/14
DTID:	<u>W45NQ900490001</u>	DEMIL:	<u>A</u>	MSDS:	
Unit of Issue:	EA	Expedited:	No		
Warehouse Location:	APLDW45NQ9000360				

Requisition History for: 2YTNUR42371410

Transaction Date	Update User	Quantity	Action	Comments
08/27/14 16:53:17	EBS		Item being processed for release and shipment. The ESD is contained in rp 70-73 when provided in response to a follow-up.	\nSales Order #: 0398112040\nRTD Screening Code: DOD
08/27/14 16:53:05	EBS		Item being processed for release and shipment. The ESD is contained in rp 70-73 when provided in response to a follow-up.	\nSales Order #: 0398112040\nRTD Screening Code: DOD
08/25/14 09:43:34	Jacob Collier	1	Request sent	Request sent to EBS
08/25/14 09:43:25	Jacob Collier	1	Approved by LESO HQ Admin	Approved by S9DS061.
08/25/14 09:42:25	Jacob Collier	1	Assigned for approval by LESO Coordinator	ASSIGNED TO S9DS061 BY S9DS061
08/25/14 09:13:35	Rolando Ayala	1	Approved by State Coordinator	Approved by ERA00143.
08/25/14 09:04:05	Blake Walls	1	Request submitted	Request submitted by EBW00315

Play Slideshow

< Previous Photo Next Photo >


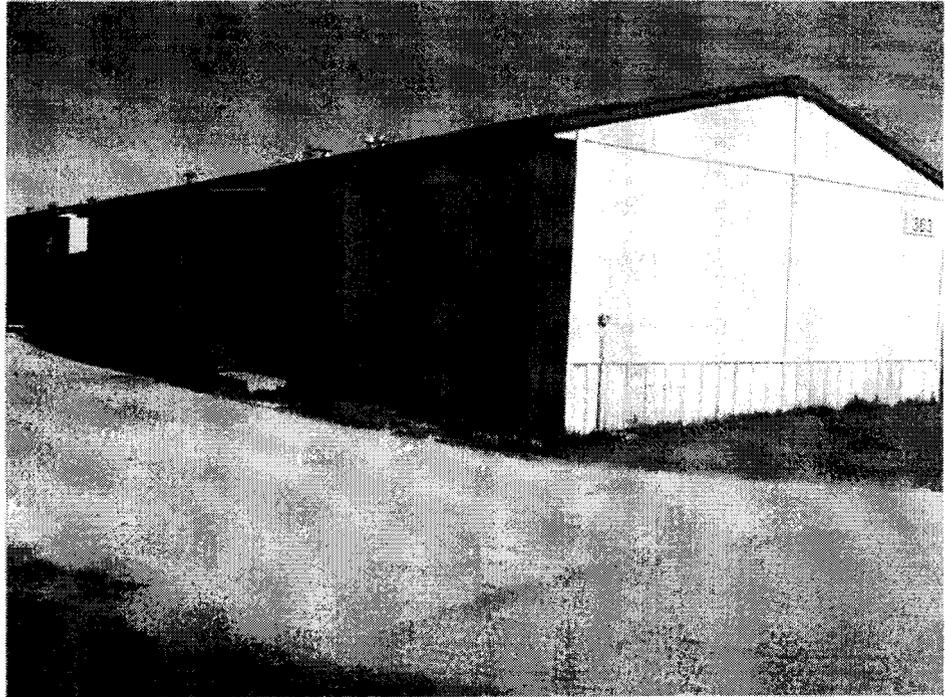


Photo 1 of 6



Disposition Services Site Added Information

PRIMARY POC: Christopher Rice
PRIMARY PHONE: 2542878822
PRIMARY EMAIL: Christopher.R.Rice@dla.mil
DRMO NAME: DLA DS HOOD

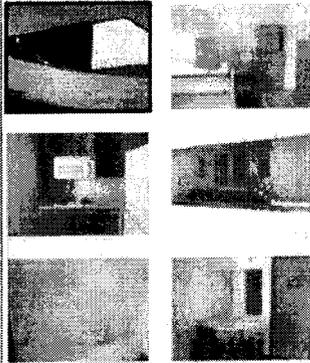

DEFENSE LOGISTICS AGENCY

Disposition Services

[Home](#) | [About Us](#) | [Public Affairs](#) | [Publications](#) | [FAQs](#) | [FOIA](#)

Reutilization / Transfer / Donation (RTD)

APD - DTID Characteristics

Show reminder

Previous Searches: 1

Announcements

Title	Description
Updated Vehicle Release Policy	Release of all types of vehicles and equipment to firefighters and law enforcement, transfer to federal agencies, donation to state and local governments, and public sale will resume as soon as property listings can be reset.
CFL Schools	All MOAs (Memorandum of Agreement) must be current (Person who sign the MOA still employed by the school) before any Computer Equipment can be received by the school under the DOD CFL PROGRAM.

LESO Shopping Cart [\[Check Out \]](#)

You Have 0 item(s) in your Shopping Cart. The Shopping Cart holds 50 items

DTID Characteristics

Inventory Information

Cycle:	<u>DOD</u>	Days Left in Cycle:	17	Hazardous:	<u>C</u>
Quantity Available:	1	Integrity Code:		Container ID:	
Condition:	<u>A</u>	Site:	<u>DLA DS HOOD</u>	Orig. Acq. Price:	1,000.00
Item Name:	PREFABRICATED AND PORTABLE BUILDINGS	NSN:	5410DSBUILDIN	Date Entered Inv.:	05/13/14
DTID:	<u>W45NQ900490001</u>	DEMIL:	<u>A</u>	MSDS:	
Unit of Issue:	EA	Expedited:	No		
Warehouse Location:	APLDW45NQ9000360				

Please perform a property search to requisition this item.

DTID W45NQ900490001 - Receipt In Place Information

DoDAAC:	W45NQ9	APLD Address Line 1:	WOVC ENGR R U ACT
APLD POC:	ZANNA.RAYNER	APLD Address Line 2:	BLDG 4408 78TH ST AT SANTA FE
APLD POC Phone:	2542879254	APLD Address Line 3:	IMWE HOD PWB SUPPLY
APLD POC Email:	ZANNA.RAYNER.CTR@MAIL.MIL	APLD Address Line 4:	FORT HOOD TX 76544-5027

APLD GPS Latitude: 000000000.000000

APLD City: FORT HOOD

APLD GPS Longitude: 000000000.000000

APLD State: TX

APLD GPS Altitude: 000000000.000000

APLD Zip: 76544

APLD Country: US

APLD Building Number: 360

DTID W45NQ900490001 - Pictures

Play Slideshow

(Previous Photo Next Photo)


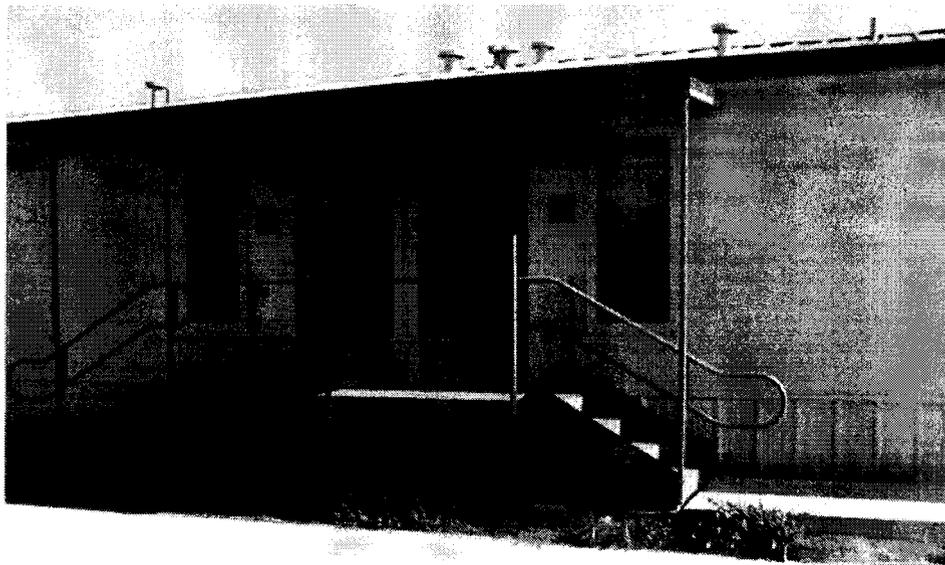


Photo 4 of 6

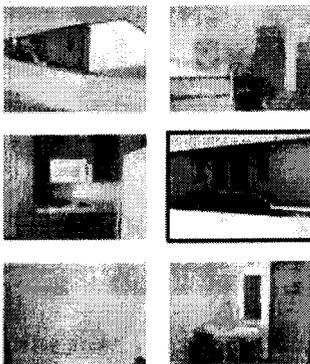

DTID W45NQ900490001 - Disposition Services Site Added Information

PRIMARY POC: Christopher Rice

PRIMARY PHONE: 2542878822

PRIMARY EMAIL: Christopher.R.Rice@dla.mil

DRMO NAME: DLA DS HOOD
